



Rail Baltica in Latvia - procurement plan and approach in 2023

Einārs Jaunzems


Director of the Project Implementation and Management Department





Project implementation progress in Latvia 2023

- Construction works ongoing in **Rail Baltica Riga Central Station section and International Airport «Riga» section**
- Ongoing design for **intermodal freight terminal**
- Ongoing design for **16 + 1 regional stations**
- Design of **infrastructure maintenance facilities** in progress
- Large scale **mainline construction** procurement (approx. 220 km) ongoing
- **A tender for the expertise of construction** projects of important Latvian Rail Baltica infrastructure facilities outside of Riga ongoing
- The development of the **railway infrastructure management model**

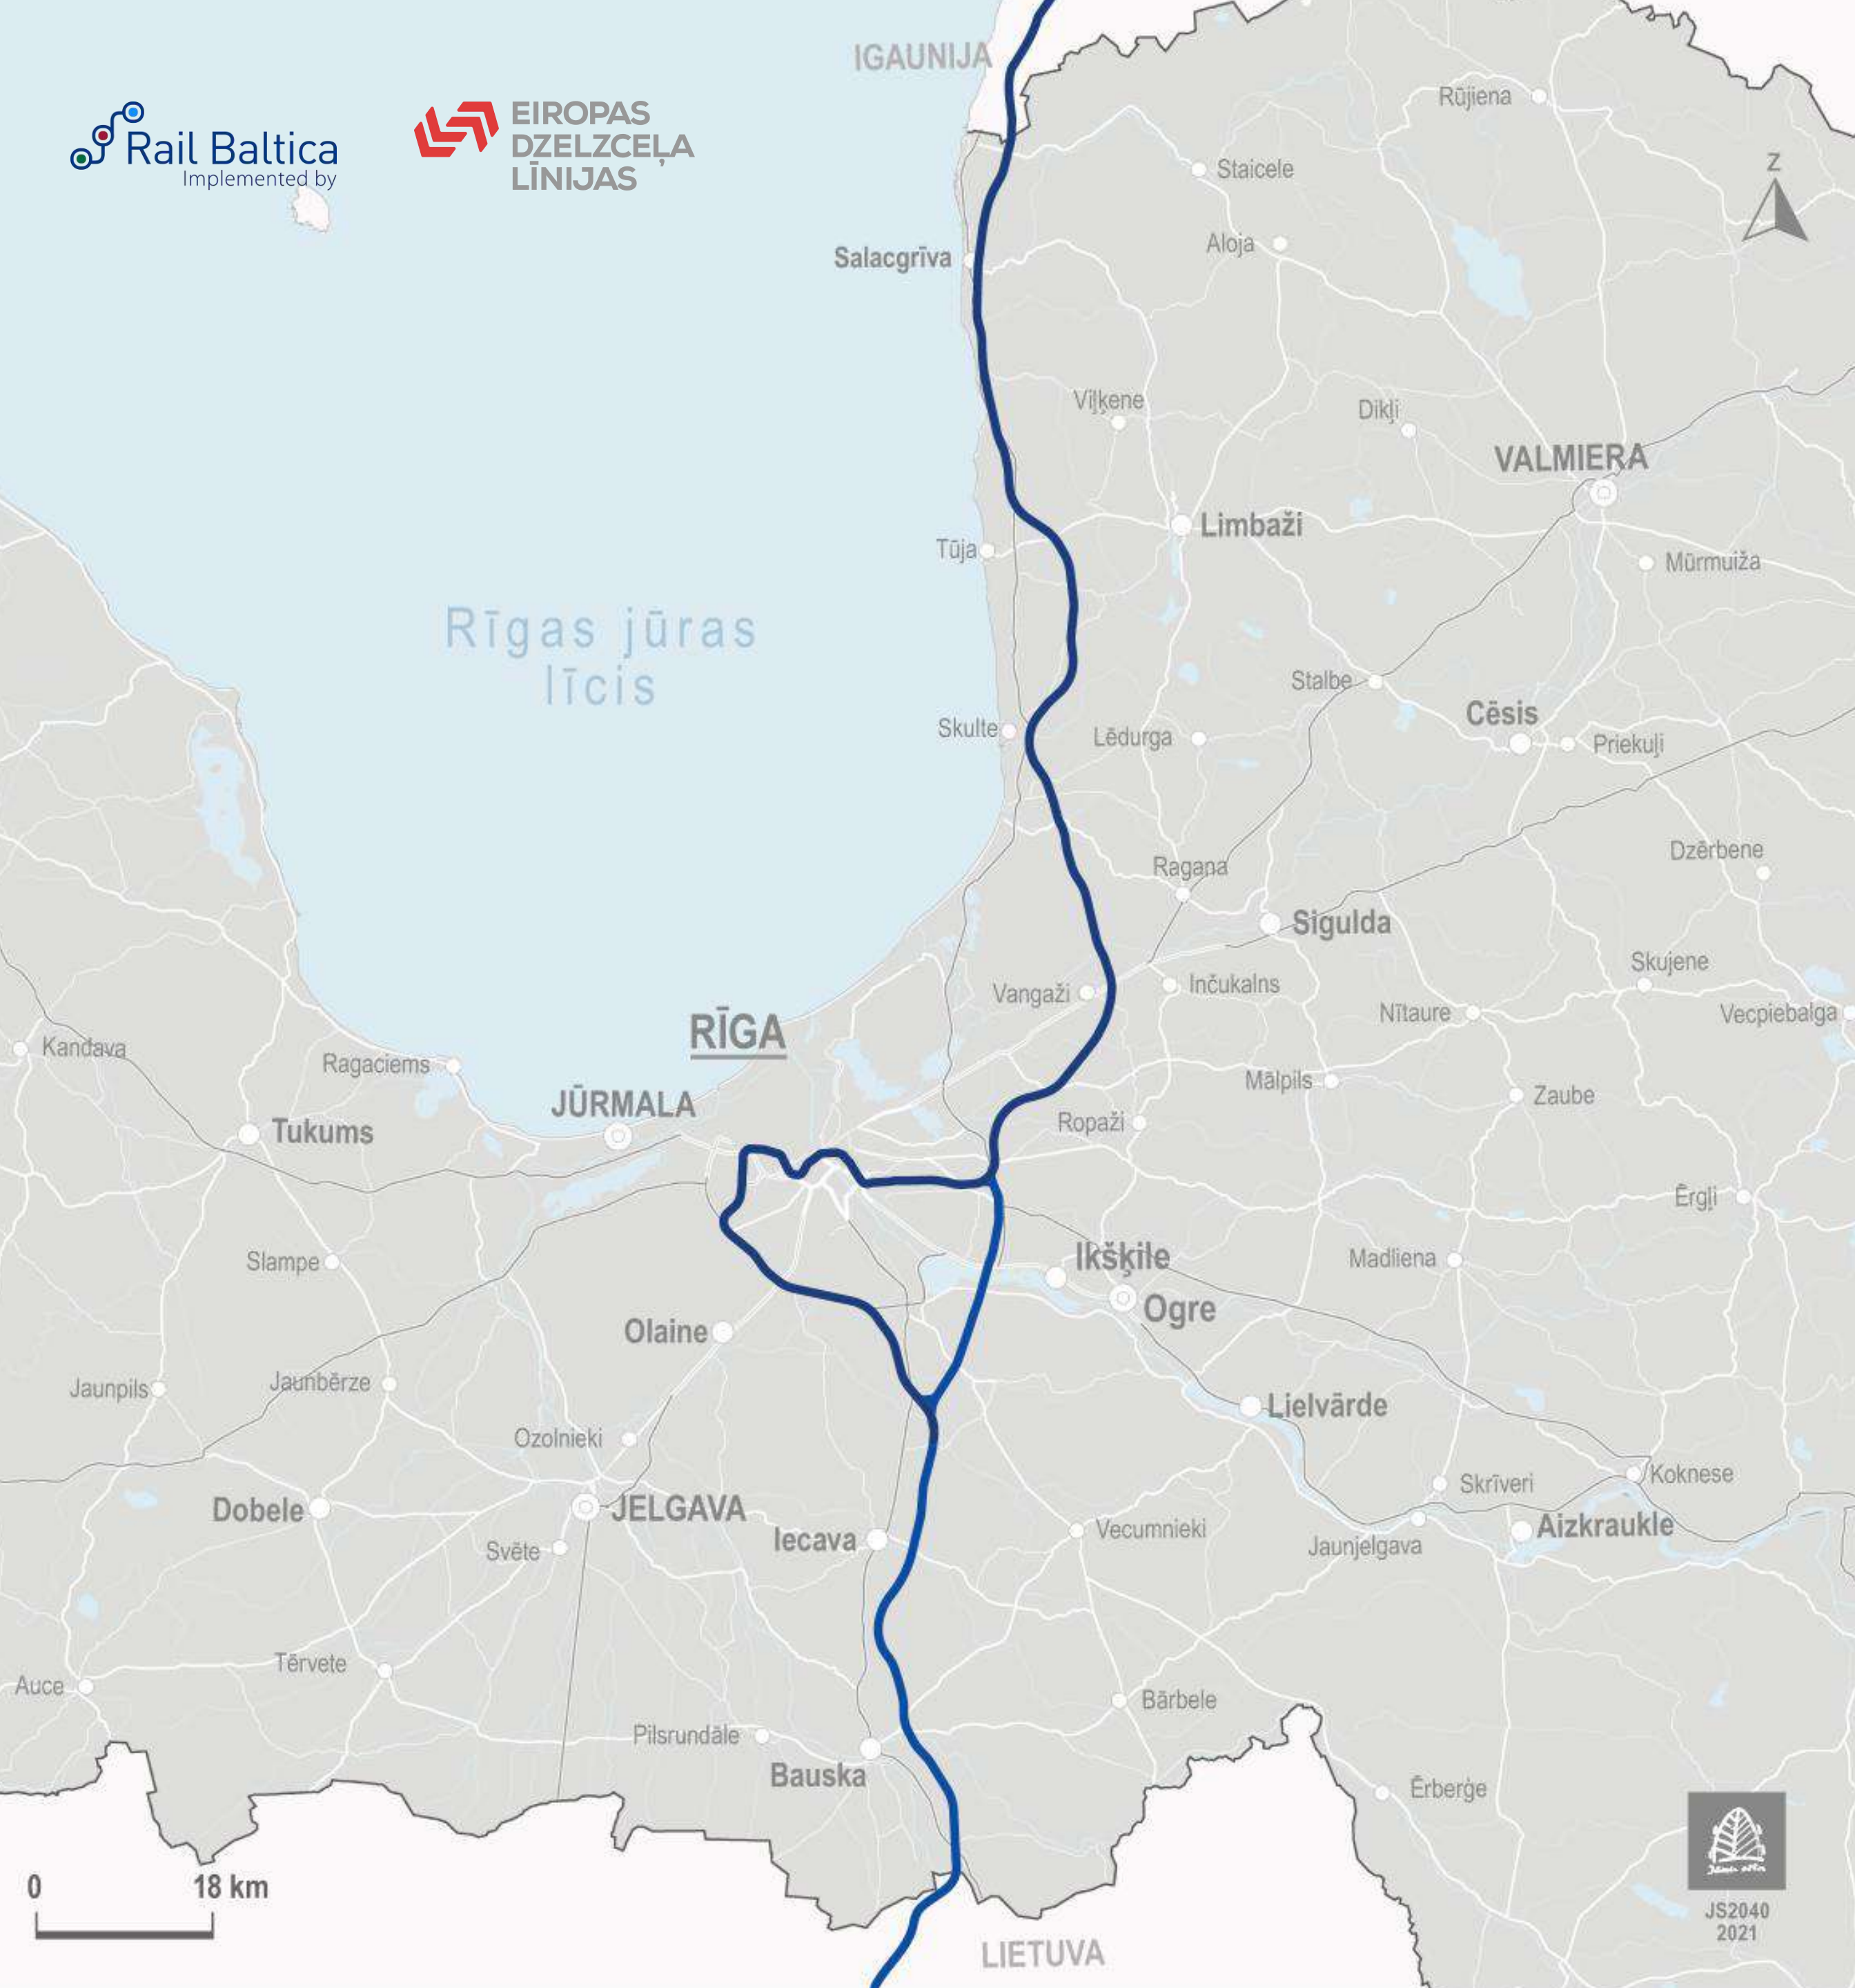

Mainline construction

Strategy

- Internationally recognized large scale contractor to be chosen
- Crossing of Riga city and borderline sections will be included in separate procurements

Construction tender

- Approx 220km
- Valuation of offers
- Contract to be signed summer 2023


Supervision tender

- Approx 220km
- Offers received
- Contract to be signed summer 2023



Upcoming **Rail Baltica** Latvia procurements 2023



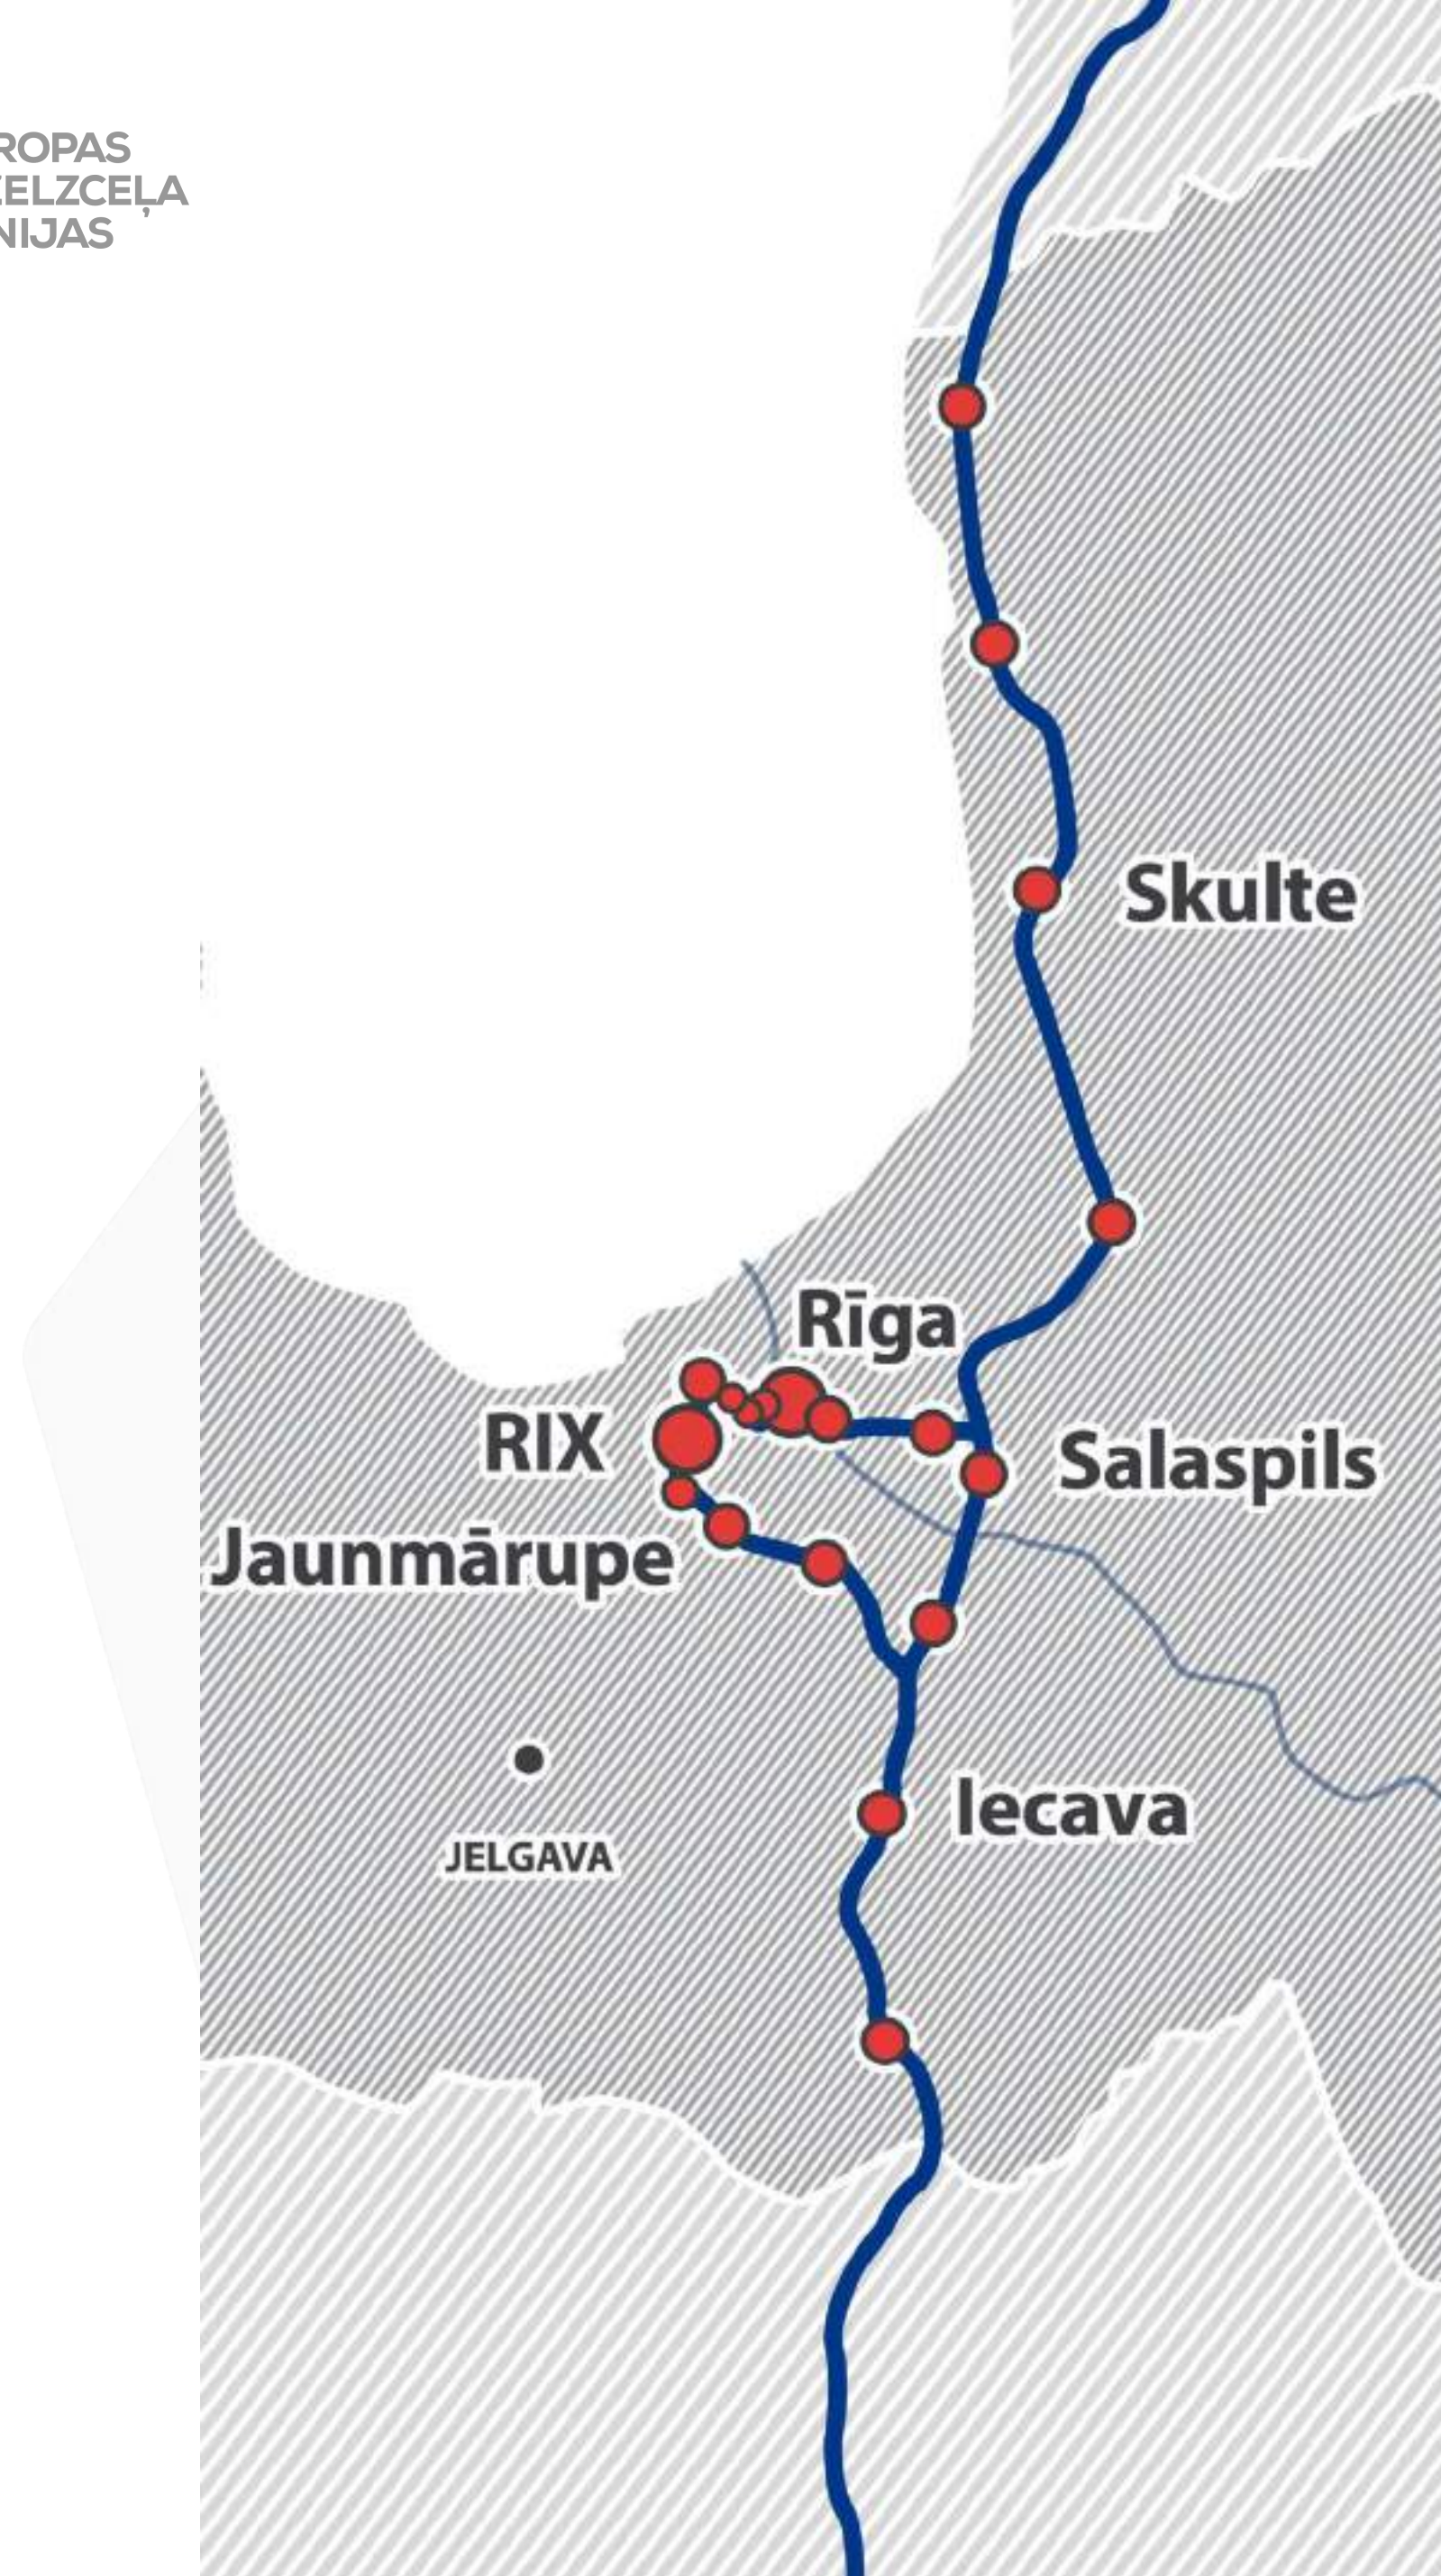

Upcoming procurements 2023

Design works of rolling stock depo in Jaunmārupe

Scope of works: Development of DTD for a rolling stock facility

Date: 07/2023

Contract to be signed: 2024

Designing of the Rail Baltica Multimodal cargo terminal at Riga Airport

Scope of works: Development of DTD for a cargo terminal with military capabilities

Date: 07/2023

Contract to be signed: 2024

Ongoing **Rail Baltica** Latvia construction works



Rail Baltica Central Station hub

Status update

- ◉ Finished column structures up to the platform beams
- ◉ Construction of the supporting elevator and stairwell up to the level of the waiting hall ongoing
- ◉ The first spans near the bus station have been built
- ◉ The planned support wall between Lāčplēša and Dzirnava streets is completed
- ◉ An overpass structure over Lāčplēša Street finished
- ◉ Several large-scale structures demolished, e.g. shopping centre Titanic, bunker
- ◉ One of the two retaining walls of the RB viaduct over the city canal was built
- ◉ The pile works on the southern side have been completed
- ◉ Project design is completed



Rail Baltica station at Riga International Airport

Status update

- Ongoing construction of station building concrete structures and railway estacade
- Air To Rail tunnel works – phase 1 completed
- New access roads under construction in total length 1990 m
- Communications relocated in total length of 40103 m;
- Piles drilled up till now – 403 (75% from all piles in section)
- Section 1 to be finished Q1 2024





Thank you!



www.edzl.lv



edzl@edzl.lv

Einārs Jaunzems

30 March 2023



Co-financed by the Connecting Europe
Facility of the European Union

